Norman Public Library Central - Mold

103 W Acres St Norman, OK 73069



Date Wed 01/10/2024

Job#

Weather

6:00 AM

30°

Clear

Wind: 12 MPH | Precipitation: .0" | Humidity: 65%

12:00 PM

47° 🧩

Clear

Wind: 12 MPH | Precipitation: .0" | Humidity: 39%

4:00 PM

57° 🌟

Clear

Wind: 12 MPH | Precipitation: .0" | Humidity: 32%

Work Logs

Name Description

City of Norman Central Library -Mold Cavins Group arrived on site and suited up in proper PPE. Upon suiting up, Cavins technicians checked all containments and equipment for defects. All air scrubber filters were changed, temperature and humidity readings were taken in all containments, all three floors in the main area, and one exterior reading. Room 311 was prepped for demo. Floor protection was put down, furniture was moved away from the demo area, cleaned, and covered.

Total

General Notes

1. Exterior: Equipment

2 - 20' Conex Boxes





2. Exterior: Temperature And Humidity



3. 303 Storage: Containment Upon Arrival/Departure





4. 303 Storage: Equipment

2 - Zip Posts





5. 305 Pioneer: Containment Upon Arrival/Departure





6. 305 Pioneer: Equipment

4 - Zip Posts









7. 311 Local History: Containment Upon Arrival/Departure




8. 311 Local History: Equipment

3 - Air Scrubbers







9. 311 Local History: Filter Change













10. 311 Local History: Temperature And Humidity



- **11.** Third Floor Main Area: Equipment
 - 1 Air Scrubber
 - 1 50' Extension Cord





12. Third Floor - Main Area: Filter Change



13. Third Floor - Main Area: Temperature And Humidity



14. 201A Staff Only: Containment Upon Arrival/Departure





15. Second Floor - Southeast Corner: Containment Upon Arrival/Departure







16. Second Floor - Southeast Corner: Equipment


22 - Zip Posts 6 - Air Scrubbers 1 - 50' Extension Cord









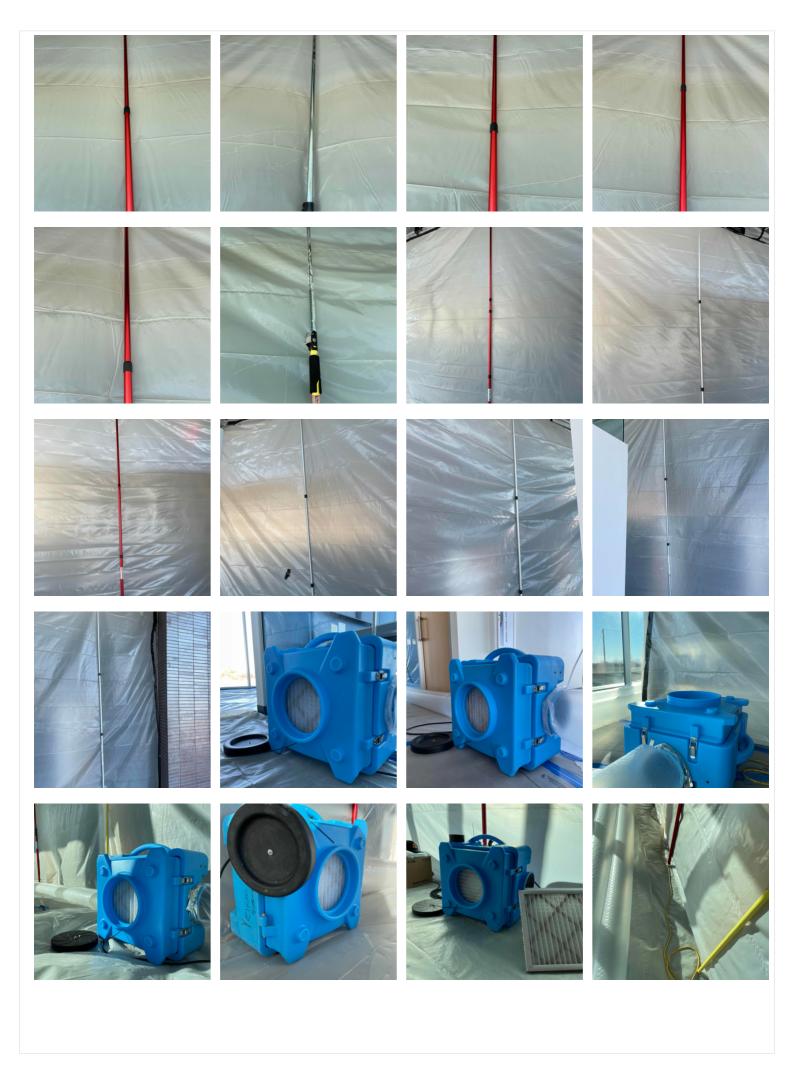







18. Second Floor - Southeast Corner: Temperature And Humidity



19. Second Floor - Main Area: Equipment

2 - Air Scrubbers 1 - 25' Extension Cord







20. Second Floor - Main Area: Filter Change





21. Second Floor - Main Area: Temperature And Humidity



22. Stairwell: Containment Upon Arrival/Departure







23. Stairwell: Equipment

- 4 Air Scrubbers
- 3 100' Extension Cords 1 Zip Post 1 Fogger



















24. Stairwell: Filter Change



25. Stairwell: Temperature And Humidity




26. 149 Storytime: Containment Upon Arrival/Departure



27. 149 Storytime: Equipment

5 - Zip Posts 2 - Air Scrubbers

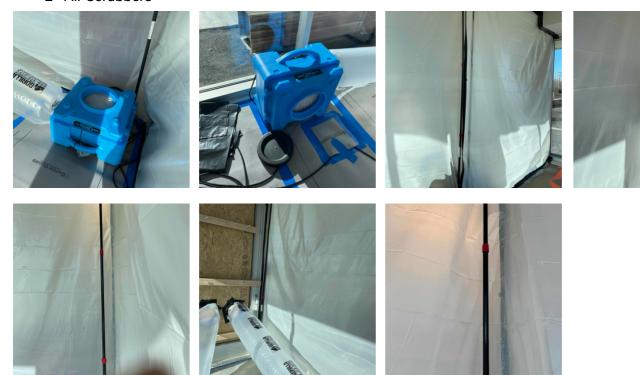

28. 149 Storytime: Filter Change



29. 149 Storytime: Temperature And Humidity



30. First Floor Main Area: Filter Change



31. First Floor Main Area: Equipment

2 - Air Scrubbers





32. First Floor Main Area: Temperature and Humidity



33. Main Entrance - Children's Area: Containment Upon Arrival/Deparure









34. First Floor - Bay Windows (Children's Area): Containment Upon Arrival/Departure







35. First Floor Southwest Vestibule: Filter Change



36. First Floor Southwest Vestibule: Temperature and Humidity



37. First Floor Southwest Vestibule: Equipment

- 2 Air Scrubbers 2 Zip Posts









38. First Floor Southwest Vestibule: Containment Upon Arrival/Departure







39. 201A Staff Only: Temperature and Humidity



40. 305 Pioneer: Temperature and Humidity



41. SO 115: Containment Upon Arrival/Departure







42. First Floor - Bay Windows (Children's Area): Temperature and Humidity




43. First Floor - Bay Windows (Children's Area): Filter Change



44. First Floor - Bay Windows (Children's Area): Equipment


12 - Zip Posts 4 - Air Scrubbers

1 - 50' Extension Cord

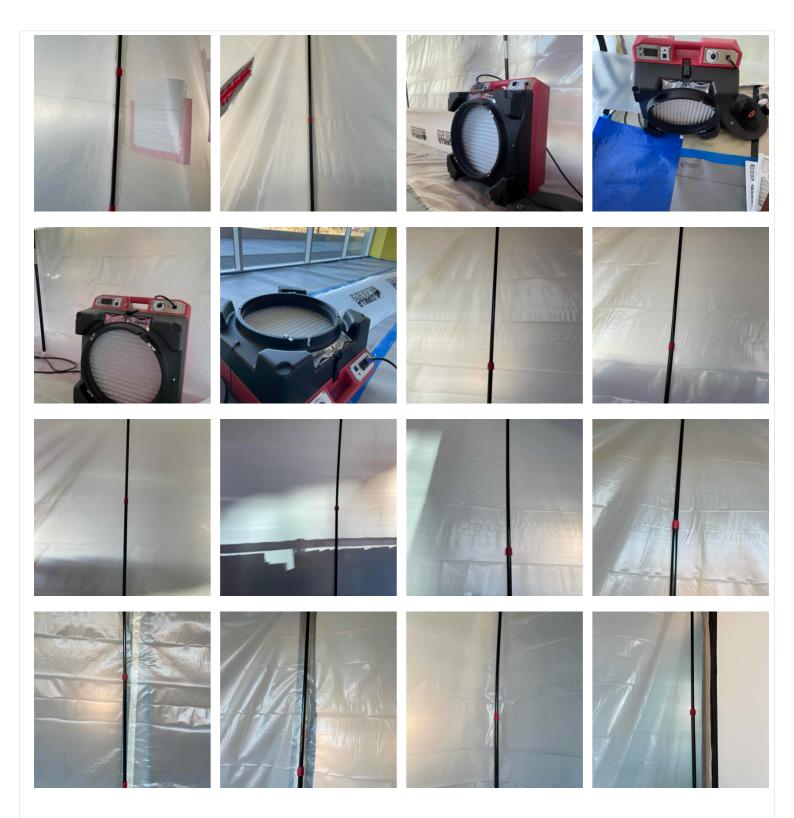

45. Main Entrance - Children's Area: Equipment

10 - Zip Post 3 - Air Scrubbers

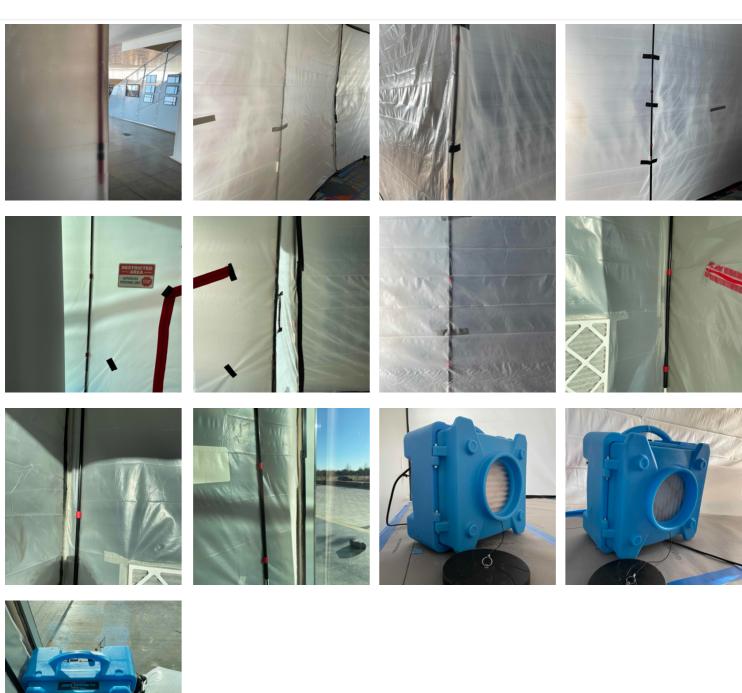



46. Main Entrance - Children's Area: Filter Change



















47. Main Entrance - Children's Area: Temperature and Humidity



48. SO 115: Equipment


- 9 Air Scrubbers 5 Hepa Vacuums 8 50' Extension
- 1 Fogger









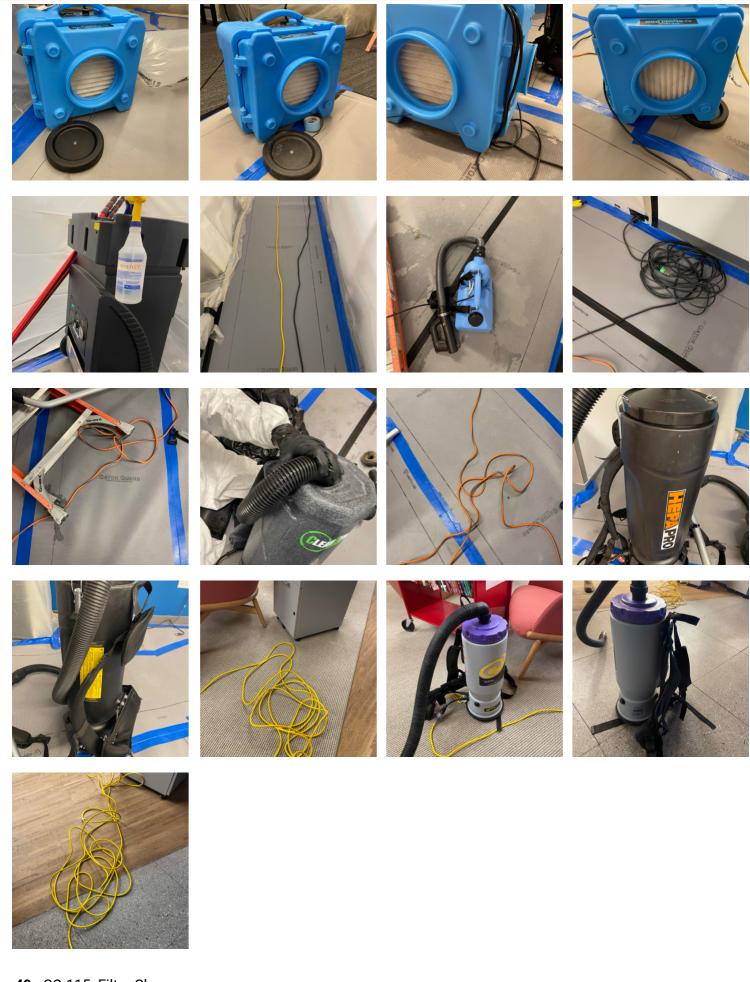

49. SO 115: Filter Change





50. SO 115: Temperature and Humidity



51. Garage: Containment Upon Arrival/Departure



52. Garage: Equipment

- 4 Air Scrubbers 2 50' Extension Cords 1 25' Extension Cord
- 2 Foggers






















53. Garage: Filter Change













54. Garage: Temperature and Humidity



55. Overall: Equipment 68 - Zip Posts 42- Air Scrubbers

5 - Hepa Vacuums


4 - Foggers 13 - 50' Extension Cords

3 - 100' Extension Cords

2 - 25' Extension Cords

56. 311 Local History: Prepare For Demo

Installed floor protection where the previous furniture was stationed, moved desk away from demo wall and cleaned and recovered with protective plastic.

















57. SO 115: Antimicrobial fog treatment















58. SO 115: Phase 1 cleaning Hepa vac ceiling, walls and floor.

