

Date Wed 02/07/2024

Job #

Weather

6:00 AM

46° 

Clear

Wind: 7 MPH | Precipitation: .0" | Humidity: 73%

12:00 PM

63° 

Clear

Wind: 20 MPH | Precipitation: .0" | Humidity: 42%

4:00 PM

64° 

Clear

Wind: 22 MPH | Precipitation: .0" | Humidity: 35%

Work Logs

Name	Description
Cavins Environmental	Cavins's technician arrived on site, suited up in proper PPE, changed all pre-filters in common areas along with temperature and humidity readings. all pre-filters and containments were changed. Spore trap testing was done in the childrens area, first floor common area, second floor common area, and on the third floor. One exterior control sample was taken as well
Total	

General Notes

1. Exterior: Equipment
2 - 20' Job Conex



2. Exterior: Temperature And Humidity



3. Third Floor - Stairwell Wall: Containment Upon Arrival/Departure





4. Third Floor - Stairwell Wall: Equipment

- 2 - Air Scrubbers
- 7 - Zip Posts
- 2 - Hepa Vacuums
- 2 - 50' Extension Cords
- 1 - Fogger












5. Third Floor - Stairwell Wall: Filter Change

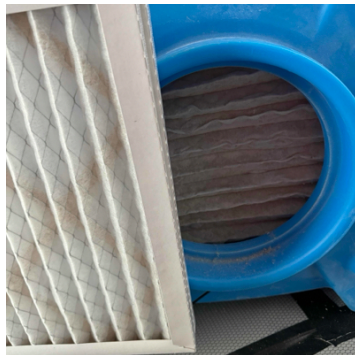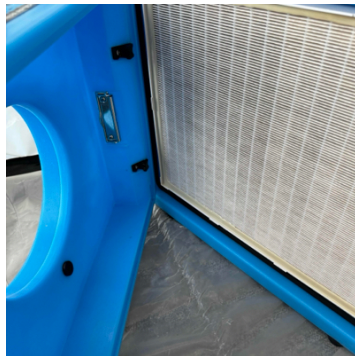


6. Third Floor - Stairwell Wall: Temperature And Humidity




7. Third Floor - Stairwell Wall: Selective Demo And Debris Hepa Vacuuming

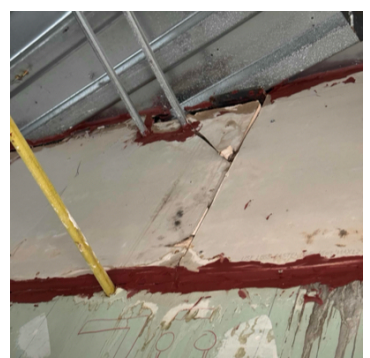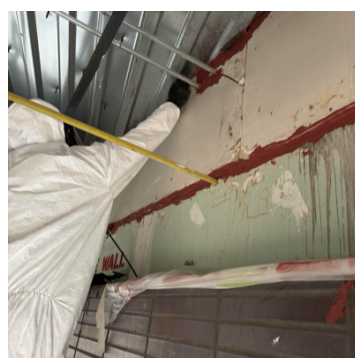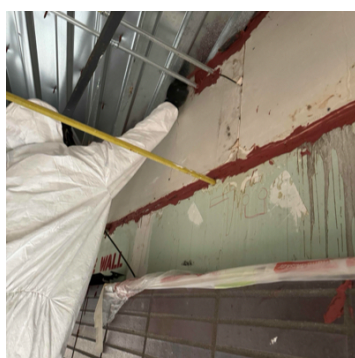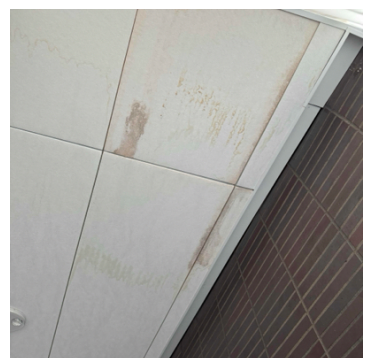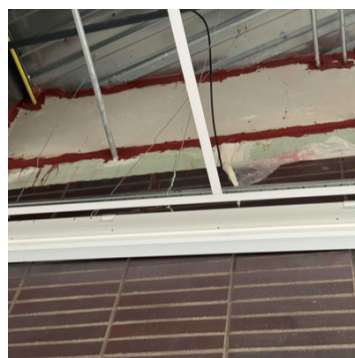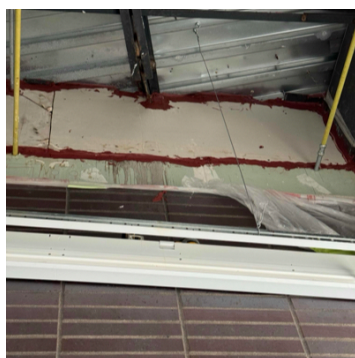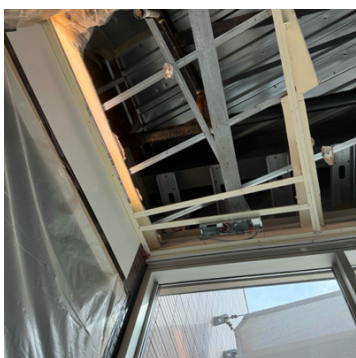


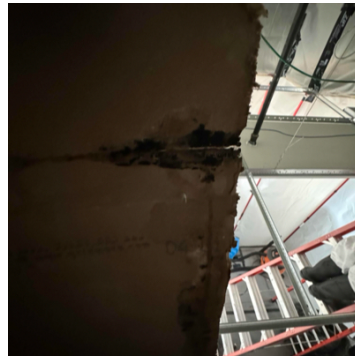


8. Third Floor - Main Area: Equipment

- 1 - Air Scrubber
- 1 - 50' Extension Cord



9. Third Floor - Main Area: Filter Change

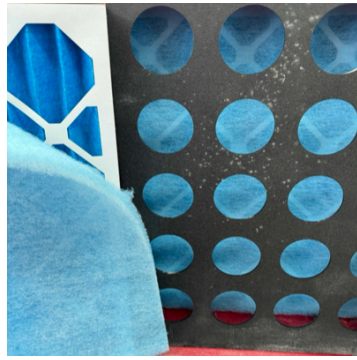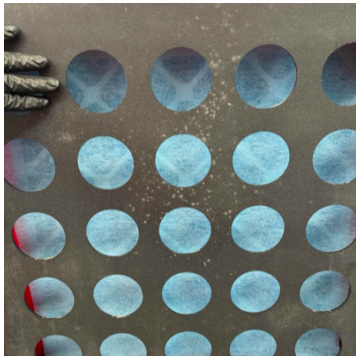




10. Third Floor - Main Area: Temperature And Humidity




11. Second Floor - Main Area: Equipment
2 - Air Scrubbers
1 - 25' Extension Cord




12. Second Floor - Main Area: Filter Change

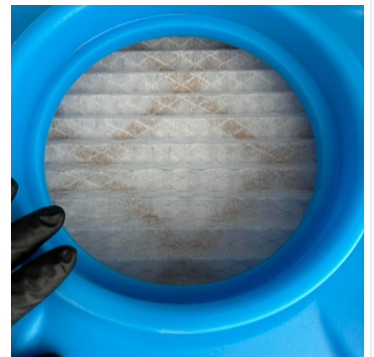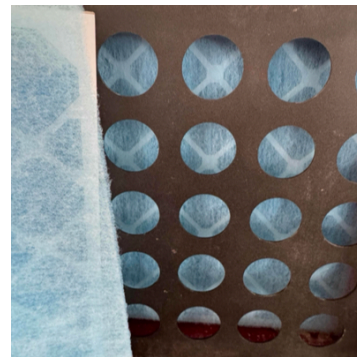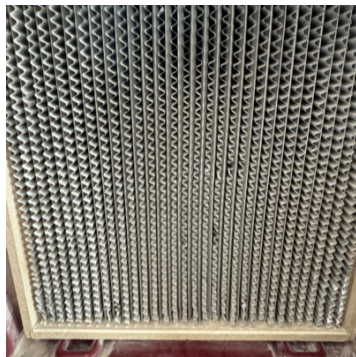

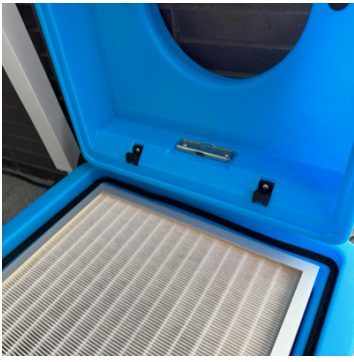

13. Third Floor - Stairwell Wall: Containment Setup

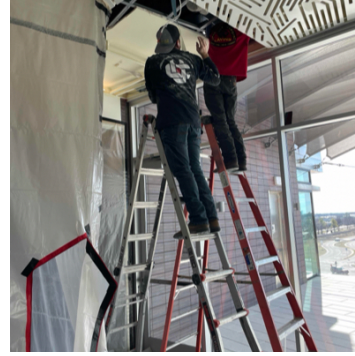

14. Second Floor - Main Area: Temperature And Humidity




15. Second Floor - Southeast Corner: Containment Upon Arrival/Departure



16. Second Floor - Southeast Corner: Equipment

- 22 - Zip Posts
- 6 - Air Scrubbers
- 2 - 50' Extension Cords



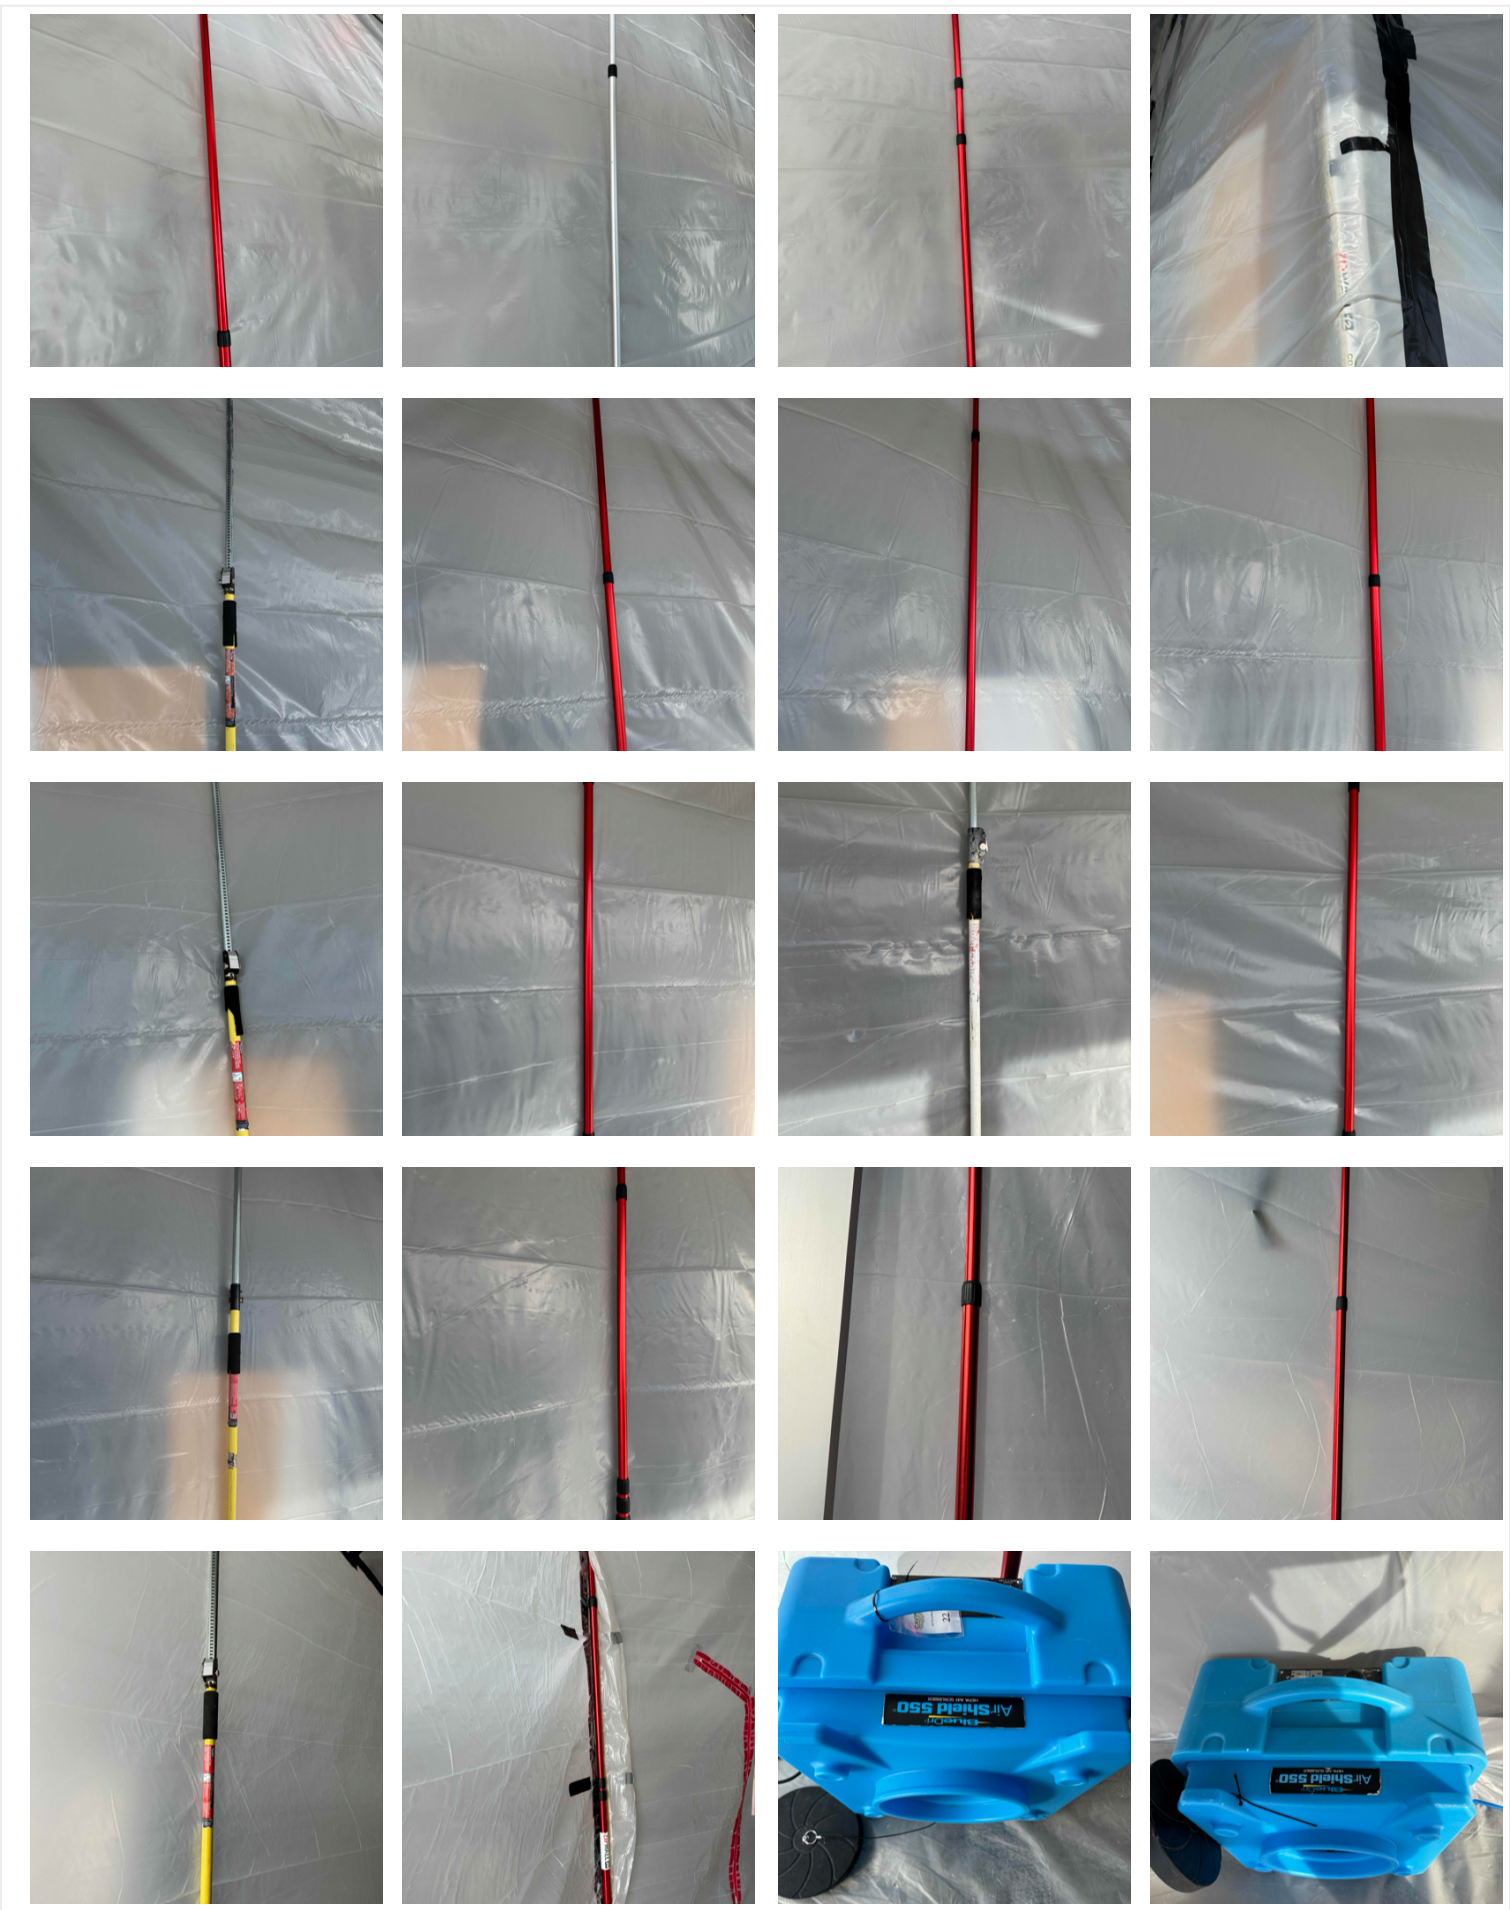



17. Second Floor - Southeast Corner: Temperature And Humidity



18. 149 Storytime: Containment Upon Arrival/Departure




19. 149 Storytime: Equipment

- 5 - Zip Posts
- 2 - Air Scrubbers
- 1 - Fogger



20. 149 Storytime: Filter Change

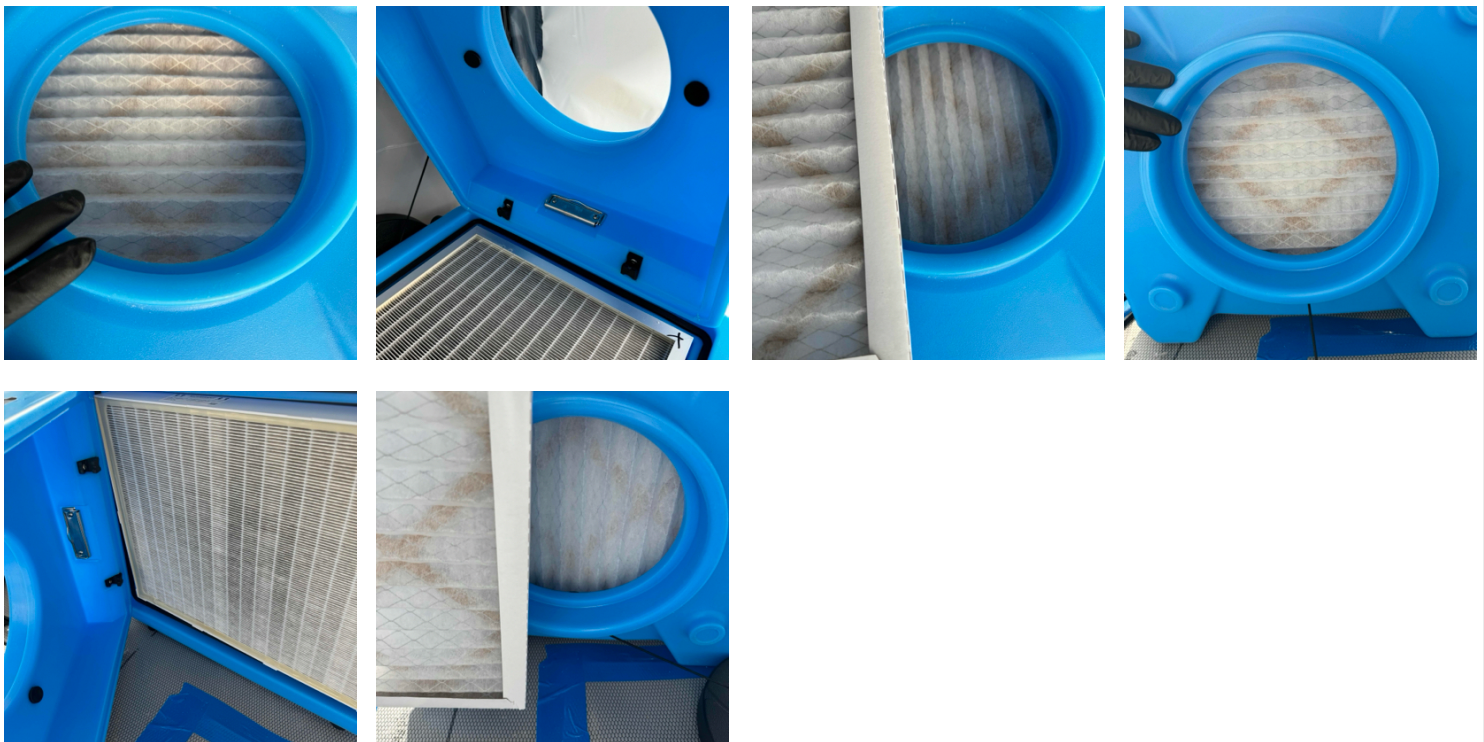

21. 149 Storytime: Temperature And Humidity




22. 149 Storytime: Anti Microbial Fog Treatment




23. First Floor - Main Area: Equipment
3 - Air Scrubbers
1 - 25' Extension Cord



24. First Floor - Main Area: Filter Change

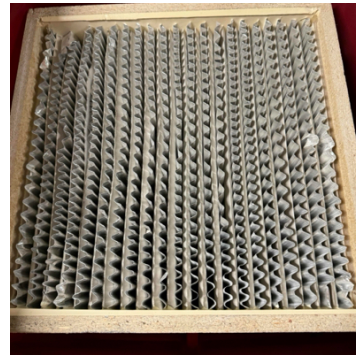

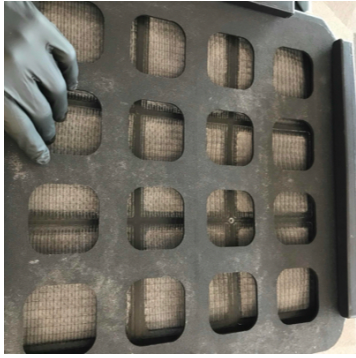

25. First Floor - Common Area Testing
One spore trap sample was taken near the staircase





26. First Floor - Main Area: Temperature And Humidity



27. Children's Area - Common Area Testin
One spore trap sample was taken.



28. Second Floor - Common Area Testing
One spore trap sample was taken.

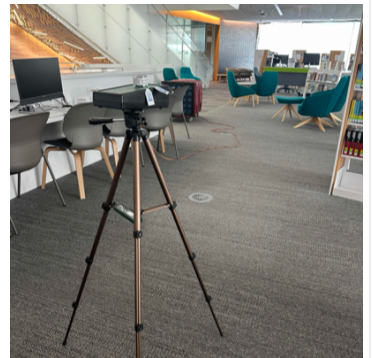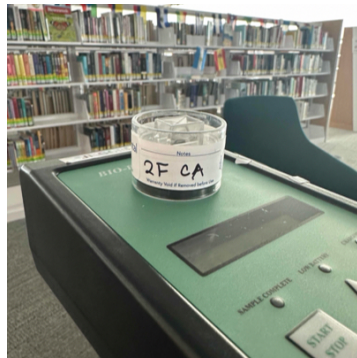

29. Third Floor - Common Area Testing
One spore trap sample was taken.



30. First Floor - Southwest Vestibule: Containment Upon Arrival/Departure



31. First Floor - Southwest Vestibule: Equipment

- 2 - Zip Posts
- 2 - Air Scrubbers
- 1 - Fogger






32. First Floor - Southwest Vestibule: Temperature And Humidity





33. First Floor - Southwest Vestibule: Anti Microbial Fog Treatment

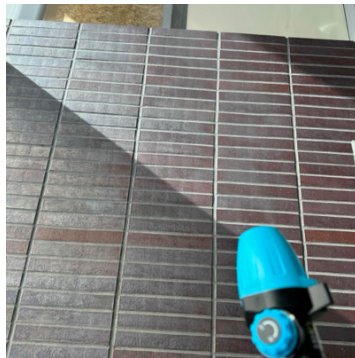

34. Second Floor - SE Corner

Post remediation verification was performed and one spore trap sample was taken.

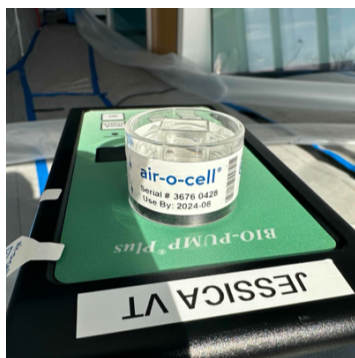
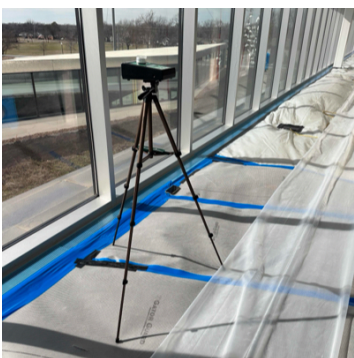


35. Testing - Exterior Control

One spore trap sample was taken.



36. First Floor - Southwest Vestibule: Filter Change

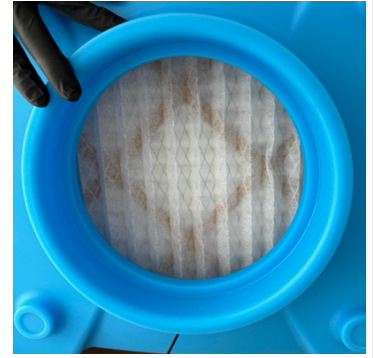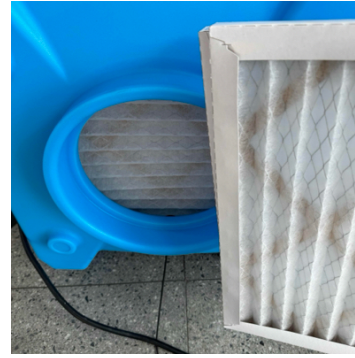

- 37. Overall: Equipment**
- 29 - Zip Posts
- 16 - Air Scrubbers
- 3 - 50' Extension Cords
- 2 - 25' Extension Cords

38. Third Floor - Stairwell Wall: Phase One Hepa Vacuuming

