

Norman Public Library Central - Mold

103 W Acres St Norman, OK 73069



Date Wed 02/14/2024

Job #

Weather

6:00 AM

39°

Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 85%

12:00 PM

63°

Clear

Wind: 19 MPH | Precipitation: .0" | Humidity: 39%

4:00 PM

68°

Clear




Wind: 29 MPH | Precipitation: .0" | Humidity: 35%

Work Logs

Name	Description
Cavins Group Environmental	Cavins technicians removed the containment on the third floor and installed the water diversion system near the SE Balcony door on the same floor. All areas of concern within the building passed clearance testing. However, air scrubbers were recommended to remain in common areas due to an upcoming visit by the envelope consultant and to maintain air quality, as the build-back has not yet been performed.
Total	

General Notes

1. Third Floor - Main Area: Equipment
1 - Air Scrubber
1 - 50' Extension Cord
2. Second Floor - Main Area: Equipment
1 - Air Scrubber
1 - 25' Extension Cord
3. First Floor - Main Area: Equipment
3 - Air Scrubbers
1 - 25' Extension Cord
4. 3rd Floor Roof Leaks
Cavins Group technicians installed leak diversion traps to address roof leaks near 3rd floor patio area.

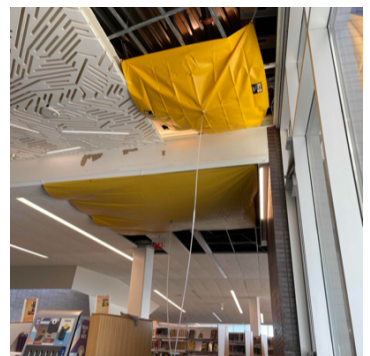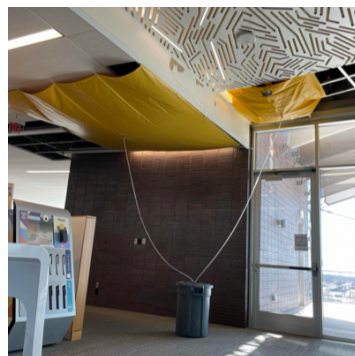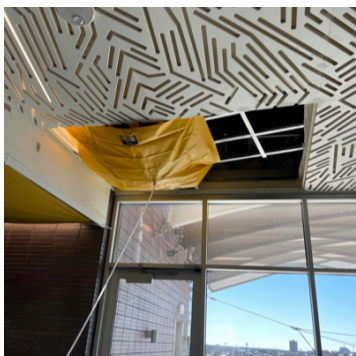

5. 3rd Floor Containment

Cavins Group technicians removed all remaining containment and equipment from 3rd floor.

